

Final Project Completion Report

Project Name and Number: **4113 South 2200 West Meter Vault Rehabilitation, #4380**

Description: The original meter station serving Granger-Hunter Improvement District (GHID) at 4113 South 2200 West was constructed in 1965 and experienced deterioration from corrosion and age-related wear. GHID designed and managed the rehabilitation project. JVWCD agreed to pay half of the construction costs via cost-share agreement.

District Project Manager: Conor Tyson

Contractor: Corrio Construction		Construction Status: 100%
Original construction contract amount:		\$213,382
Total Change Order amount:		\$34,540
Final construction contract amount:		\$247,922
JVWCD Share (50%)		\$123,961
Total change orders as a percentage of original contract:		16.2%
Completion Schedule:		
Notice to Proceed:		3/17/2025
Final Completion:		8/5/2025

Summary of Change Orders:		
	Description	Amount
1	Addition of steel reducers	\$13,914
2	Stainless steel valve	\$1,494
3	Additional electrical work	\$8,612
4	Vault lid modifications	\$3,068
5	Reimbursemetn of permit fees	\$6,200
6	Expidited PRV shipping and electrical	\$1,252
	Total Change Order Amount:	\$34,540
	JVWCD Share (50%):	\$17,270

Final Project Completion Report



Excavating the vault and piping



Vault with piping and lid removed




New piping attached to pipeline with thrust block being formed



New meter and valves in vault



Backfilling and compacting over vault

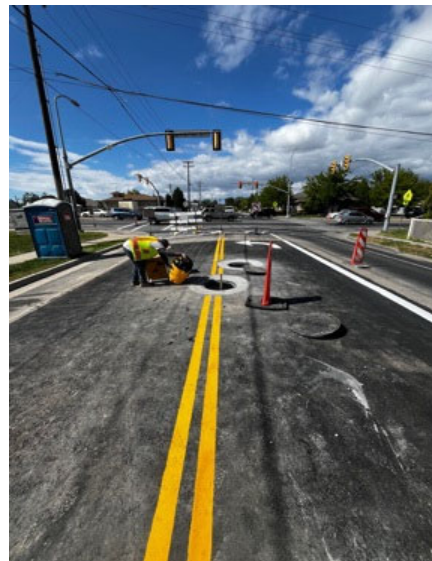

Restored road over vault
