

Final Project Completion Report

Project Name and Number: **5200 West 6200 South Reservoir, #4231**

Description: Design and construction of a concrete, rectangular, 6.8 million gallon reservoir at the 5200 West 6200 South reservoir site in West Jordan, Utah. In 1962, the original 2 million gallon reservoir was constructed and this new reservoir works in conjunction with it. The new reservoir will provides redundancy to the northwest area of JVVCD's system and supports the growing demands of GHID, KID, TBID, MID, Hexcel, and West Jordan.

District Project Manager: Travis Christensen

Engineer: Bowen Collins & Associates	Design Status: 100%
Original Engineering Contract Amount:	\$940,526
Final Engineering Contract Amount:	\$986,210

Contractor: Ralph L Wadsworth Construction	Construction Status: 100%
Original construction contract amount:	\$15,522,920
Total Change Order amount:	
Final construction contract amount:	\$15,613,579
Total change orders as a percentage of original contract:	0.6%
Completion Schedule:	
Notice to Proceed:	7/7/2023
Final Completion:	10/15/2025

Summary of Change Orders:		Amount
	Description	
1	Site screening, drain modification, and debris removal	\$19,255
2	Wash down water piping reroute and addition of access ladder	\$10,672
3	New gaskets for existing flow control valve and electrical equipment	\$28,826
4	Reservoir site modifications to grading, landscaping, and railings	\$73,658
5	Raising of existing vault hatch and irrigation controller upgrades	\$20,248
6	Installation of wire in conduits for security cameras	\$3,570
7	Miscellaneous closeout items	\$8,088
	Total Change Order Amount:	\$164,317

Final Project Completion Report



Preparation of reservoir subgrade




Setting forms and rebar for reservoir floor



Concrete columns and walls



Concrete roof panels being poured

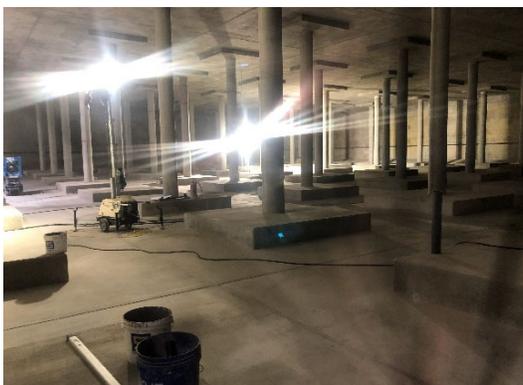

Interior of the finished reservoir



Final grading and reservoir access road
